



Turn-Key Environmental Consultants, Inc.

790 Barnhart Rd.
Troy, OH 45373

714 Monument Ave.
Dayton, OH 45402

Phone: 937-335-8807
Fax: 937-339-4882

August 28, 2015

Mr. Dennis Zimmer
City of Dayton, Division of Housing Inspection
371 West Second Street, 3rd Floor
Dayton, Ohio 45402

RE: Comprehensive Pre-Demolition Asbestos Survey, NOP TK-7amended, Vacant Residence, 3848 Merrimac Ave., Dayton, OH, TKEC Project #TK-7aH

Dear Mr. Zimmer:

On August 14, 2015, Mr. Joseph Saunders (Ohio Department of Health Certified Asbestos Hazard Evaluation Specialist #ES34837) of Turn-Key Environmental Consultants, Inc. (TKEC) visited the vacant residence located at 3848 Merrimac Ave. in Dayton, Ohio (subject property). The purpose of the visit was to perform a pre-demolition asbestos survey of the structure to identify asbestos containing materials (ACMs) located in the structure prior to demolition activities being performed.

EXECUTIVE SUMMARY

On August 14, 2015, Mr. Joseph Saunders (Ohio Department of Health Certified Asbestos Hazard Evaluation Specialist # ES34837) of Turn-Key Environmental Consultants, Inc. (TKEC) performed a comprehensive pre-demolition asbestos inspection of the vacant residence located at 3848 Merrimac Ave. in Dayton, Ohio. Twelve (12) samples of suspect materials were collected from the residential structure. The samples were shipped overnight to an accredited laboratory for analysis. Some of the samples were comprised of layers which resulted in the analysis of a total of twenty (20) samples. Laboratory analysis indicated that one (1) sample contained 1% or greater asbestos. One (1) sample of window glazing contained 2% asbestos. This sample was subsequently analyzed by EPA PLM 400 Point Count. This sample was determined to contain 0.5% chrysotile asbestos and will not need to be abated.

No other suspect materials were observed in the structure that will require abatement.

DESCRIPTION OF BUILDING SURVEY AND SAMPLING METHODOLOGY

A room-by-room inspection of the house was performed and homogenous materials were identified. Sampling locations were determined in a statistically random manner for surfacing materials, or randomly distributed manner for thermal system insulation that is representative of the homogeneous area. Each bulk sample was collected using cleaned hand tools and placed in a clean, zip-lock plastic bag and labeled with a unique sample identification number. Pertinent information was recorded on a Bulk Sample Log Sheet, including sample identification number, date of collection, name of inspector, building name, a brief description and location of the sample, and the type of material sampled (e.g. thermal insulation, fireproofing, acoustical plaster). The samples were shipped via overnight courier to SanAir Technologies Laboratory, Inc. (SanAir), an accredited and recognized laboratory under the National Voluntary Laboratory Accreditation Program (NVLAP) and analyzed for asbestos content by polarized-light microscopy (PLM) and dispersion staining (Method Reference: EPA-600/R-93/116). This analytical method, which the EPA currently recommends for the determination of asbestos in bulk samples of suspect material can be used for qualitative identification of six (6) morphologically different types of asbestos fibers: chrysotile, amosite, crocidolite, anthophyllite, tremolite and actinolite asbestos.

The method specifies that the asbestos content in a bulk sample shall be estimated and reported as a finite percentage (rounded to the nearest percentage) within the range of 0 to 100. The result of the bulk sample analysis is reported in a standard written laboratory report. This report includes the clients name, the project number, the laboratory identification number, the sample number assigned to the bulk sample upon receipt at the laboratory, and the field number assigned to the bulk sample upon collection. If the bulk sample contains more than one distinct layer of material, each layer is analyzed separately. The composition of the bulk sample is reported in percentages of asbestos and non-asbestos components. A summary of the bulk samples collected from this structure is included in Table 1 – Bulk Sample Log.

One (1) sample of window glazing contained 2% asbestos. This sample was subsequently analyzed by EPA PLM 400 Point Count. This sample was determined to contain 0.5% chrysotile asbestos and will not need to be abated.

The results of the sample analyses can be found on the laboratory report attached and in Table 2 – Bulk Sample Data Summary. Table 2 also contains the locations, condition, amount, NESHAP category and type of ACM identified in the structure.

RESULTS

TKEC collected samples from wall and ceiling systems, flooring materials, roofing materials, duct insulation, blown-in insulation and window glaze and caulking if it was present. Analytical results confirmed that none of the suspect asbestos-containing building materials contain more than 1% asbestos:

No other suspect asbestos-containing building materials that will likely become friable during demolition were identified in the structure.

ESTIMATED ABATEMENT COSTS

TKEC estimates the costs associated with the removal of the confirmed asbestos-containing materials to be as follows:

The estimated costs for asbestos consulting (specifications and on-site monitoring) if requested by the City of Dayton: N/A

ESTIMATED COSTS FOR FRIABLE ACM ABATEMENT

<u>Material</u>	<u>Estimated Quantity</u>	<u>Estimated Unit Costs</u>	<u>Estimated Costs</u>
N/A	N/A	N/A	N/A

The estimated costs for asbestos consulting (specifications and on-site monitoring): \$ N/A

ESTIMATED COSTS FOR NON-FRIABLE ACM LIKELY TO BECOME FRIABLE ABATEMENT

<u>Material</u>	<u>Estimated Quantity</u>	<u>Estimated Unit Costs</u>	<u>Estimated Costs</u>
N/A	N/A	N/A	N/A

The estimated costs for asbestos consulting (specifications and on-site monitoring) if requested by the City of Dayton: N/A

ESTIMATED COSTS FOR NON-FRIABLE ACM ABATEMENT

<u>Material</u>	<u>Estimated Quantity</u>	<u>Estimated Unit Costs</u>	<u>Estimated Costs</u>
N/A	N/A	N/A	N/A

The estimated costs for asbestos consulting (specifications and on-site monitoring) if requested by the City of Dayton: N/A

Estimated costs are based on prevailing costs in the Midwest for 2015, and do not include costs for planning, permitting, contractor oversight or air monitoring. Actual costs may vary from estimated costs due to contractor workloads, season, or changes in regulatory requirements.

RECOMMENDATIONS

Based on the findings of this asbestos survey and NESHAP regulations, the following recommendations are presented for consideration:

1. Prior to any outside contractor(s) working at the subject structure, the contractor(s) must be notified of the presence of the building materials identified as containing asbestos.
2. Trained workers and supervisors certified by the Ohio Department of Health must be used to remove the identified asbestos-containing building materials using special procedures and protective equipment to ensure that workers are not overexposed to airborne asbestos.
3. Advance notification must be provided to the Regional Air Pollution Control Agency (RAPCA) and the Ohio Department of Health at least ten (10) working days prior to the start of abatement activities.
4. The fact that asbestos containing materials were observed in or on the building should be noted on the demolition notification form along with the name and certification number of the inspector (Joseph D. Saunders, Ohio Department of Health Asbestos Hazard Evaluation Specialist Certification No. ES34837).


TKEC made every effort to locate suspect ACM that may be concealed; however, suspect ACM which may be located behind hard plaster walls or ceilings, hard walled chases, under flooring or subflooring, etc., were not assessed or quantified. If through demolition suspect materials are discovered, they should be documented and handled appropriately.

3848 Merrimac Ave.
August 28, 2015

This report is prepared to assist the City of Dayton, construction managers and asbestos abatement contractors in locating ACMs. This report is not intended to be used as a bidding document or project specifications.

Attached are the following TKEC documents: 1) Table I – Bulk Sample Log; 2) Table 2 – Bulk Sample Data Summary; 3) Laboratory Report; 4) Building Sketch/Photographs; and 5) Inspector’s Certification. If we can be of further assistance on this or other projects, do not hesitate to call us at (937) 335-8807.

Respectfully submitted,
TURN-KEY ENVIRONMENTAL CONSULTANTS, INC.

A handwritten signature in cursive script that reads "Joseph Saunders".

Joseph Saunders
Project Manager
ODH Asbestos Hazard Evaluation Specialist
No. ES34837, Exp. Date 6/10/2016

ATTACHMENT 1

Bulk Sample Log

ATTACHMENT 2

Bulk Sample Data Summary

3848 Merrimac Ave.
 Pre-Demolition Asbestos Survey
 Table I - Bulk Sample Data Summary
 Project: TK-7aH

Homogeneous Area					Quantity & Condition			
Sample Description (Material Type)	Sample Location	NSHAP Category	ACM Type	Bulk Sample No.	Good	Fair	Poor	Asbestos Content
Drywall/Plaster/Skim Coat - Drywall	Living Room			1-1				NAD
Drywall/Plaster/Skim Coat - Plaster	Living Room			1-1				NAD
Drywall/Plaster/Skim Coat - Skim Coat	Living Room			1-1				NAD
Drywall/Plaster/Skim Coat - Drywall	Bedroom 1			1-2				NS
Drywall/Plaster/Skim Coat - Plaster	Bedroom 1			1-2				NAD
Drywall/Plaster/Skim Coat - Skim Coat	Bedroom 1			1-2				NAD
Drywall/Plaster/Skim Coat - Drywall	Bedroom 2			1-3				NS
Drywall/Plaster/Skim Coat - Plaster	Bedroom 2			1-3				NAD
Drywall/Plaster/Skim Coat - Plaster	Bedroom 2			1-3				NAD
Drywall/Plaster/Skim Coat - Skim Coat	Bedroom 2			1-3				NAD
Drywall/Plaster/Skim Coat - Drywall	Kitchen			1-4				NAD
Drywall/Plaster/Skim Coat - Plaster	Kitchen			1-4				NAD
Drywall/Plaster/Skim Coat - Skim Coat	Kitchen			1-4				NAD

3848 Merrimac Ave.
 Pre-Demolition Asbestos Survey
 Table I - Bulk Sample Data Summary
 Project: TK-7aH

Homogeneous Area					Quantity & Condition			
Sample Description (Material Type)	Sample Location	NSHAP Category	ACM Type	Bulk Sample No.	Good	Fair	Poor	Asbestos Content
Drywall/Texture - Drywall	Living Room			1-5				NAD
Drywall/Texture - Plaster	Living Room			1-5				NS
Drywall/Texture - Skim Coat	Living Room			1-5				NS
Drywall/Texture - Texture	Living Room			1-5				NAD
Floor Tile 12"	Bathroom			2-1				NAD
Window Glazing	Kitchen			3-1				2% Chrysotile
Window Glazing	Porch			3-2				NAD
Flooring/Mastic - Floor Tile	Kitchen			4-1				NAD
Flooring/Mastic - Mastic	Kitchen			4-1				NAD
Linoleum	Under Sink			5-1				NAD
Roof Shingle	Roof			6-1				NAD
Ceiling Tile	Basement			7-1				NAD

3848 Merrimac Ave.
 Pre-Demolition Asbestos Survey
 Table I - Point Count Sample Data Summary
 Project: TK-7aH

Homogeneous Area					Quantity & Condition			
Sample Description (Material Type)	Sample Location	NSHAP Category	ACM Type	Bulk Sample No.	Good	Fair	Poor	Asbestos Content
Window Glazing	Kitchen			3-1				0.5% Chrysotile

ATTACHMENT 3

Laboratory Data

SanAir Technologies Laboratory

Analysis Report

prepared for

**Turn-Key Environmental
Consultants, Inc.**

Report Date: 8/25/2015
Project Name: 3848 Merrimac
Project #: TK-7aH
SanAir ID#: 15025195



NVLAP LAB CODE 200870-0



Certification # 652931



License # LAB0166



804.897.1177

www.sanair.com



SanAir Technologies Laboratory, Inc.

1551 Oakbridge Drive, Suite B, Powhatan, VA 23139
804.897.1177 Toll Free: 888.895.1177 Fax: 804.897.0070
Web: <http://www.sanair.com> E-mail: iaq@sanair.com

SanAir ID Number

15025195

FINAL REPORT

Name: Turn-Key Environmental Consultants, Inc.
Address: 790 Barnhart Road
Troy, OH 45373

Project Number: TK-7aH
P.O. Number:
Project Name: 3848 Merrimac

Collected Date: 8/14/2015
Received Date: 8/18/2015 9:50:00 AM
Report Date: 8/25/2015 6:00:53 PM
Analyst: Robertson, Erin

Asbestos Bulk PLM EPA 600/R-93/116

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
1-1 / 15025195-001 Drywall/ Plaster/ Skim Coat Living Room, Drywall	Off-White Non-Fibrous Homogeneous	5% Cellulose	95% Other	None Detected
1-1 / 15025195-001 Drywall/ Plaster/ Skim Coat Living Room, Plaster	Grey Non-Fibrous Homogeneous		100% Other	None Detected
1-1 / 15025195-001 Drywall/ Plaster/ Skim Coat Living Room, Skim Coat	White Non-Fibrous Homogeneous		100% Other	None Detected

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
1-2 / 15025195-002 Drywall/ Plaster/ Skim Coat Bed 1, Drywall				Not Submitted
1-2 / 15025195-002 Drywall/ Plaster/ Skim Coat Bed 1, Plaster	Grey Non-Fibrous Homogeneous		100% Other	None Detected
1-2 / 15025195-002 Drywall/ Plaster/ Skim Coat Bed 1, Skim Coat	White Non-Fibrous Homogeneous		100% Other	None Detected

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
1-3 / 15025195-003 Drywall/ Plaster/ Skim Coat Bed 2, Drywall				Not Submitted
1-3 / 15025195-003 Drywall/ Plaster/ Skim Coat Bed 2, Plaster	Grey Non-Fibrous Homogeneous		100% Other	None Detected
1-3 / 15025195-003 Drywall/ Plaster/ Skim Coat Bed 2, Skim Coat	White Non-Fibrous Homogeneous		100% Other	None Detected
1-3 / 15025195-003 Drywall/ Plaster/ Skim Coat Bed 2, Texture	Various Non-Fibrous Heterogeneous		100% Other	None Detected

Certification

Signature: 
Date: 8/25/2015

Reviewed: 
Date: 8/25/2015



SanAir Technologies Laboratory, Inc.

1551 Oakbridge Drive, Suite B, Powhatan, VA 23139
804.897.1177 Toll Free: 888.895.1177 Fax: 804.897.0070
Web: <http://www.sanair.com> E-mail: iaq@sanair.com

SanAir ID Number

15025195

FINAL REPORT

Name: Turn-Key Environmental Consultants, Inc.
Address: 790 Barnhart Road
Troy, OH 45373

Project Number: TK-7aH
P.O. Number:
Project Name: 3848 Merrimac

Collected Date: 8/14/2015
Received Date: 8/18/2015 9:50:00 AM
Report Date: 8/25/2015 6:00:53 PM
Analyst: Robertson, Erin

Asbestos Bulk PLM EPA 600/R-93/116

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
1-4 / 15025195-004 Drywall/ Plaster/ Skim Coat Kitchen, Drywall	Off-White Non-Fibrous Homogeneous	5% Cellulose	95% Other	None Detected
1-4 / 15025195-004 Drywall/ Plaster/ Skim Coat Kitchen, Plaster	Grey Non-Fibrous Homogeneous		100% Other	None Detected
1-4 / 15025195-004 Drywall/ Plaster/ Skim Coat Kitchen, Skim Coat	White Non-Fibrous Homogeneous		100% Other	None Detected

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
1-5 / 15025195-005 Drywall/ Texture Living Room Ceiling, Drywall	Off-White Non-Fibrous Homogeneous	5% Cellulose	95% Other	None Detected
1-5 / 15025195-005 Drywall/ Texture Living Room Ceiling, Plaster				Not Submitted
1-5 / 15025195-005 Drywall/ Texture Living Room Ceiling, Skim Coat				Not Submitted
1-5 / 15025195-005 Drywall/ Texture Living Room Ceiling, Texture	Off-White Non-Fibrous Homogeneous		100% Other	None Detected

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
2-1 / 15025195-006 12" Floor Tile Bath	White Non-Fibrous Homogeneous		100% Other	None Detected

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
3-1 / 15025195-007 Window Glazing Kitchen Window	Various Non-Fibrous Heterogeneous		98% Other	2% Chrysotile

Certification

Signature: 
Date: 8/25/2015

Reviewed: 
Date: 8/25/2015



SanAir Technologies Laboratory, Inc.

1551 Oakbridge Drive, Suite B, Powhatan, VA 23139
804.897.1177 Toll Free: 888.895.1177 Fax: 804.897.0070
Web: <http://www.sanair.com> E-mail: iaq@sanair.com

SanAir ID Number

15025195

FINAL REPORT

Name: Turn-Key Environmental Consultants, Inc.
Address: 790 Barnhart Road
Troy, OH 45373

Project Number: TK-7aH
P.O. Number:
Project Name: 3848 Merrimac

Collected Date: 8/14/2015
Received Date: 8/18/2015 9:50:00 AM
Report Date: 8/25/2015 6:00:53 PM
Analyst: Robertson, Erin

Asbestos Bulk PLM EPA 600/R-93/116

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
3-2 / 15025195-008 Window Glazing Porch Window	White Non-Fibrous Homogeneous		100% Other	None Detected

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
4-1 / 15025195-009 Flooring Entire Kitchen (12x18), Flooring	Green Non-Fibrous Homogeneous		100% Other	None Detected
4-1 / 15025195-009 Flooring Entire Kitchen (12x18), Mastic	Yellow Non-Fibrous Homogeneous		100% Other	None Detected

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
5-1 / 15025195-010 Linoleum Under Sink In Kitchen	Orange Non-Fibrous Heterogeneous		100% Other	None Detected

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
6-1 / 15025195-011 Roof Roof	Grey Non-Fibrous Heterogeneous	15% Glass	85% Other	None Detected

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
7-1 / 15025195-012 Ceiling Tile Basement	White Fibrous Homogeneous	80% Cellulose	20% Other	None Detected

Certification

Signature: 
Date: 8/25/2015

Reviewed: 
Date: 8/25/2015



1551 Oakbridge Drive Suite B
 Powhatan, VA 23139
 804-897-1177 / 888-895-1177
 Fax 804-897-0070
 www.sanair.com

**Asbestos
Chain of Custody**

SanAir ID Number
 15025195

Company: Turn-Key Environmental Consultants, Inc.		Project #: TK-7a.1t	Collected by: J. Saunders
Address: 790 BarnHart Rd.		Project Name: 3848 Merrimac	Phone #: 937-335-8807
City, St., Zip: Troy, OH 45373		Date Collected: 8/14/15	Fax #:
State of Collection: Ohio	Account#:	P.O. Number:	Email: TKEC@Turn-keyenvironmental.com

Bulk		Air		Soil/Vermiculite	
ABB	PLM EPA 600/R-93/116 <input checked="" type="checkbox"/>	ABA	PCM NIOSH 7400 <input type="checkbox"/>	ABSE	PLM EPA 600/R-93/116 (Qual.) <input type="checkbox"/>
	Positive Stop <input type="checkbox"/>	ABA-2	OSHA w/ TWA* <input type="checkbox"/>	ABSP	PLM CARB 435 (LOD <1%) <input type="checkbox"/>
ABEPA	PLM EPA 400 Point Count <input type="checkbox"/>	ABTEM	TEM AHERA <input type="checkbox"/>	ABSP1	PLM CARB 435 (LOD 0.25%) <input type="checkbox"/>
ABB1K	PLM EPA 1000 Point Count <input type="checkbox"/>	ABATN	TEM NIOSH 7402 <input type="checkbox"/>	ABSP2	PLM CARB 435 (LOD 0.1%) <input type="checkbox"/>
ABBEN	PLM EPA NOB <input type="checkbox"/>	ABT2	TEM Level II <input type="checkbox"/>		
ABBCH	TEM Chatfield <input type="checkbox"/>				
ABBTM	TEM EPA NOB <input type="checkbox"/>				
Water		New York ELAP		Dust	
ABHE	EPA 100.2 <input type="checkbox"/>	PLM NY	PLM EPA 600/M4-82-020 <input type="checkbox"/>	ABWA	TEM Wipe ASTM D-6480 <input type="checkbox"/>
		ABEPA2	NY ELAP 198.1 <input type="checkbox"/>	ABDMV	TEM Microvac ASTM D-5755 <input type="checkbox"/>
		ABENY	NY ELAP 198.6 PLM NOB <input type="checkbox"/>		
		ABBNY	NY ELAP 198.4 TEM NOB <input type="checkbox"/>	Matrix	Other <input type="checkbox"/>

Turn Around Times	3 HR (4 HR TEM) <input type="checkbox"/>	6 HR (8HR TEM) <input type="checkbox"/>	12 HR <input type="checkbox"/>	24 HR <input type="checkbox"/>
	2 Days <input type="checkbox"/>	3 Days <input type="checkbox"/>	4 Days <input type="checkbox"/>	5 Days <input checked="" type="checkbox"/>

Special Instructions

Sample #	Sample Identification/Location	Volume or Area	Sample Type	Flow Rate*	Time* Start - Stop
	(See Attached Bulk Sample Log)				

Relinquished by	Date	Time	Received by	Date	Time
J. Saunders	8/17/15	1700	MC	AUG 18 2015	9:50AM

Unless scheduled, the turn around time for all samples received after 3 pm EST Friday will begin at 8 am Monday morning. Weekend or Holiday work must be scheduled ahead of time and is charged for rush turn around time. Work with standard turn around time sent Priority Overnight and Billed to Recipient will be charged a \$10 shipping fee. Page 1 of 1

SanAir Technologies Laboratory

Analysis Report

prepared for

**Turn-Key Environmental
Consultants, Inc.**

Report Date: 8/28/2015
Project Name: 3848 Marrimac
Project #: TK-7aH
SanAir ID#: 15026334



NVLAP LAB CODE 200870-0



Certification # 652931



License # LAB0166



804.897.1177

www.sanair.com



SanAir Technologies Laboratory, Inc.

1551 Oakbridge Drive, Suite B, Powhatan, VA 23139
804.897.1177 Toll Free: 888.895.1177 Fax: 804.897.0070
Web: <http://www.sanair.com> E-mail: iaq@sanair.com

SanAir ID Number

15026334

FINAL REPORT

Name: Turn-Key Environmental Consultants, Inc.
Address: 790 Barnhart Road
Troy, OH 45373

Project Number: TK-7aH
P.O. Number:
Project Name: 3848 Marrimac

Collected Date: 8/14/2015
Received Date: 8/26/2015 8:00:00 AM
Report Date: 8/28/2015 11:44:51 AM
Analyst: Robertson, Erin

Asbestos Bulk EPA PLM 400 Point Count

SanAir ID / Description	Stereoscopic Appearance	Components		Asbestos Fibers
		% Fibrous	% Non-Fibrous	
3-1 / 15026334-001 Window Glazing Kitchen Window	Various Non-Fibrous Heterogeneous		99.5% Other	0.5% Chrysotile

Certification

Signature: 
Date: 8/28/2015

Reviewed: 
Date: 8/28/2015

15026334

Maria E. Coker

From: Sandra C. Sobrino
Sent: Wednesday, August 26, 2015 11:15 AM
To: Maria E. Coker
Cc: Jonathan G. Tallert
Subject: FW: Point Count Analyses

400 point count.

Sandra Sobrino

From: Turn-Key Environmental [mailto:tkec@turn-keyenvironmental.com]
Sent: Tuesday, August 25, 2015 9:30 PM
To: Sandra C. Sobrino <ssobrino@sanair.com>
Subject: Point Count Analyses

Dear Sandra,

Please run EPA PLM 499 Point Count analysis on the following samples:

TK-7aB -
15025205-001
15025205-002
15025205-004

TK-7aC -
15025209-001
15025209-003

TK-7aD -
15025207-001
15025207-002
15025207-003
15025207-004

TK-7aG -
15025199-001
15025199-002
15025199-003

TK-7aH - 15025195-007

TK-7aI -
15025204-001
15025204-002
15025204-003
15025204-004
15025204-005

TK-7aJ -

15026334

15025198-003
15025198-004

TK-7aK -
15025197-001
15025197-002
15025197-003
15025197-004
15025197-005
15025197-006
15025197-007
15025197-012
15025197-013

If possible, I would like 2 day TAT.

Thank you,

Joe Saunders

--

Turn-Key Environmental Consultants, Inc.
790 Barnhart Road
Troy, Ohio 45373
937-335-8807
www.turn-keyenvironmental.com

15026334



1551 Oakbridge Drive Suite B
Powhatan, VA 23139
804-897-1177 / 888-895-1177
Fax 804-897-0070
www.sanair.com

Asbestos
Chain of Custody

SanAir ID Number
15025195

Company: Turn-Key Environmental Consultants, Inc.	Project #: <i>TK-Fault</i>	Collected by: J. Saunders
Address: 790 BarnHart Rd.	Project Name: <i>3848 Merrimac</i>	Phone #: 937-335-8807
City, St., Zip: Troy, OH 45373	Date Collected: <i>8/14/15</i>	Fax #:
State of Collection: Ohio Account#:	P.O. Number:	Email: TKEC@Turn-keyenvironmental.com

Bulk			Air			Soil/Vermiculite		
ABB	PLM EPA 600/R-93/116	<input checked="" type="checkbox"/>	ABA	PCM NIOSH 7400	<input type="checkbox"/>	ABSE	PLM EPA 600/R-93/116 (Qual.)	<input type="checkbox"/>
	Positive Stop	<input type="checkbox"/>	ABA-2	OSHA w/ TWA*	<input type="checkbox"/>	ABSP	PLM CARB 435 (LOD <1%)	<input type="checkbox"/>
ABEPA	PLM EPA 400 Point Count	<input type="checkbox"/>	ABTEM	TEM AHERA	<input type="checkbox"/>	ABSP1	PLM CARB 435 (LOD 0.25%)	<input type="checkbox"/>
ABB1K	PLM EPA 1000 Point Count	<input type="checkbox"/>	ABATN	TEM NIOSH 7402	<input type="checkbox"/>	ABSP2	PLM CARB 435 (LOD 0.1%)	<input type="checkbox"/>
ABBEN	PLM EPA NOB	<input type="checkbox"/>	ABT2	TEM Level II	<input type="checkbox"/>			
ABBCH	TEM Chatfield	<input type="checkbox"/>						
ABBTM	TEM EPA NOB	<input type="checkbox"/>						
Water			New York ELAP			Dust		
ABHE	EPA 100.2	<input type="checkbox"/>	PLM NY	PLM EPA 600/M4-82-020	<input type="checkbox"/>	ABWA	TEM Wipe ASTM D-6480	<input type="checkbox"/>
			ABEPA2	NY ELAP 198.1	<input type="checkbox"/>	ABDMV	TEM Microvac ASTM D-5755	<input type="checkbox"/>
			ABENY	NY ELAP 198.6 PLM NOB	<input type="checkbox"/>	Matrix	Other	<input type="checkbox"/>
			ABBNY	NY ELAP 198.4 TEM NOB	<input type="checkbox"/>			

Turn Around Times	3 HR (4 HR TEM) <input type="checkbox"/>	6 HR (8HR TEM) <input type="checkbox"/>	12 HR <input type="checkbox"/>	24 HR <input type="checkbox"/>
	2 Days <input type="checkbox"/>	3 Days <input type="checkbox"/>	4 Days <input type="checkbox"/>	5 Days <input checked="" type="checkbox"/>

Special Instructions


Sample #	Sample Identification/Location	Volume or Area	Sample Type	Flow Rate*	Time* Start - Stop
	(See Attached Bulk Sample Log)				

Relinquished by	Date	Time	Received by	Date	Time
<i>J. Saunders</i>	<i>8/17/15</i>	<i>1700</i>	<i>MC</i>	<i>AUG 18 2015</i>	<i>9:50AM</i>

Unless scheduled, the turn around time for all samples received after 3 pm EST Friday will begin at 8 am Monday morning. Weekend or Holiday work must be scheduled ahead of time and is charged for rush turn around time. Work with standard turn around time sent Priority Overnight and Billed to Recipient will be charged a \$10 shipping fee.

ATTACHMENT 4

Site Sketch/Photographs

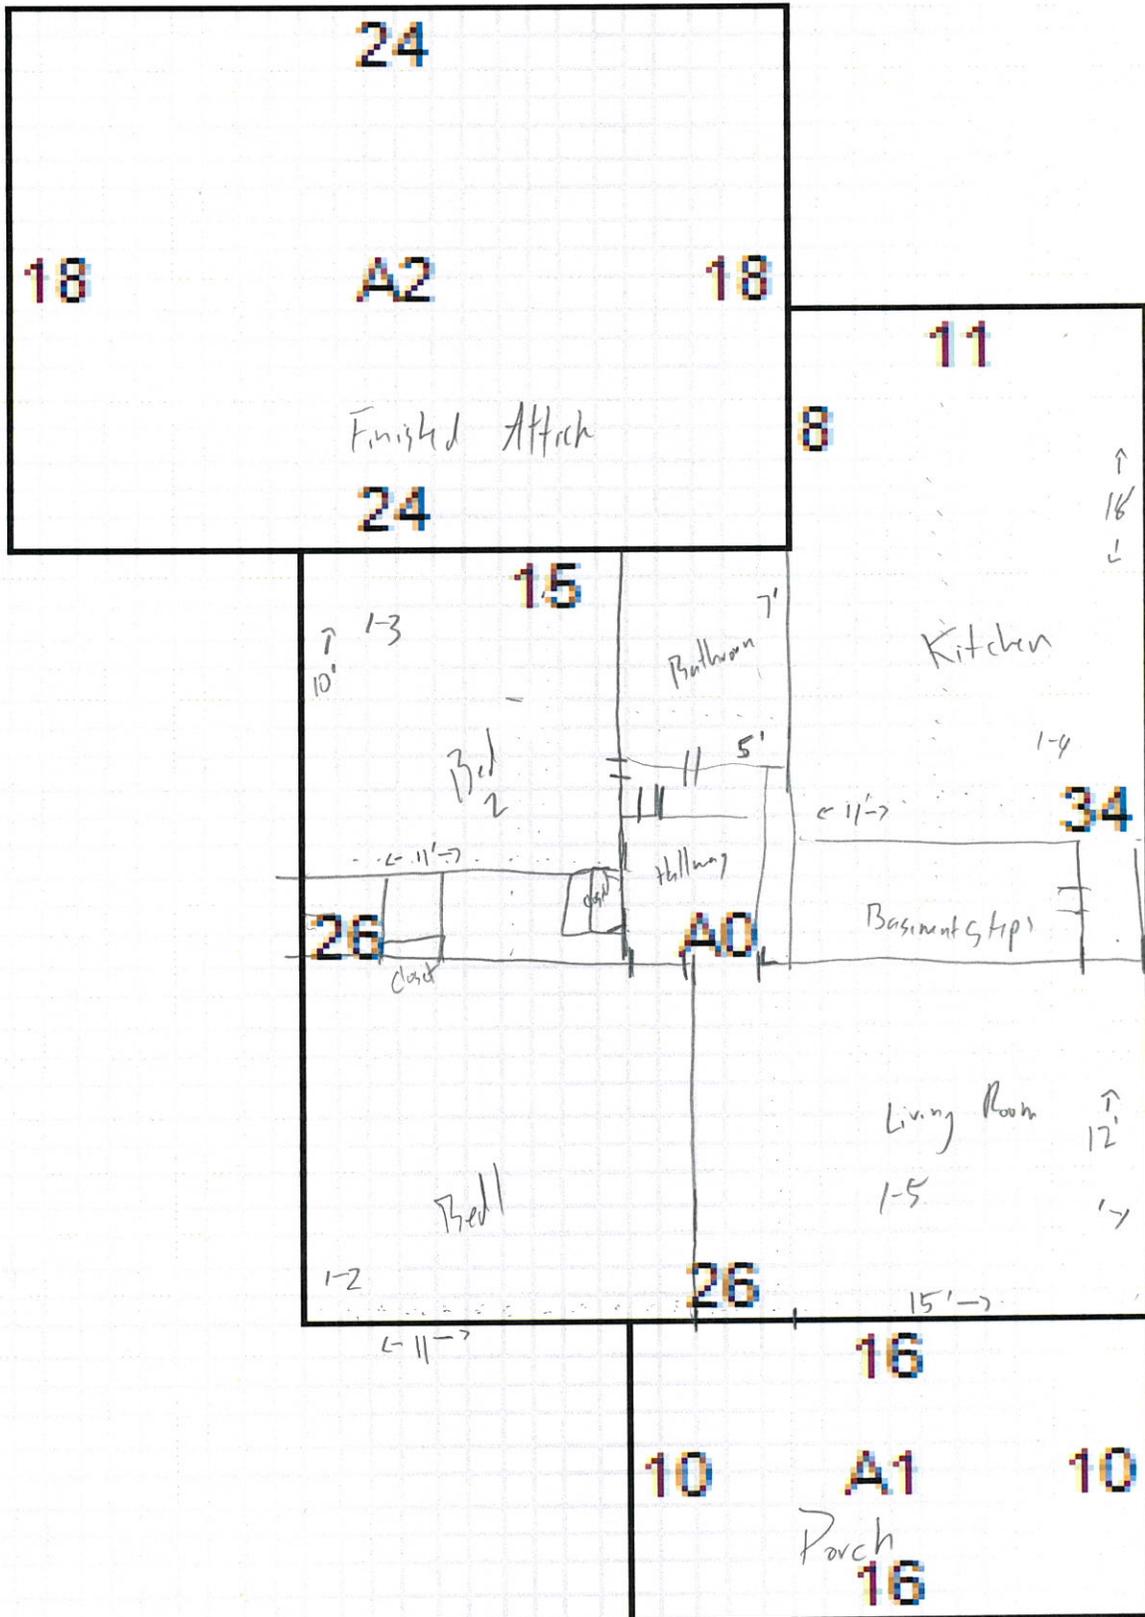

1-1 Approximate
Sample Location

1-1* Asbestos > 1%

Floor 1

3848 Merrimac Ave.

TK-7aH



3848 Merrimac



Sample 1-1 Drywall/Plaster/Skim Coat



Sample 1-2 Drywall/Plaster/Skim Coat



Sample 1-3 Drywall/Plaster/Skim Coat



Sample 1-4 Drywall/Plaster/Skim Coat



Sample 1-5 Drywall/Texture



Sample 2-1 12" Floor Tile



Sample 3-1 Window Glazing



Sample 3-2 Window Glazing



Sample 4-1 Flooring



Sample 5-1 Linoleum Flooring



Sample 7-1 Ceiling Tile

ATTACHMENT 5

Inspector's Certification



TSI Training Services International

Asbestos Building Inspector Refresher

Certificate

This is to certify

Joseph D. Saunders

XXXX-XX-6484



has attended and successfully completed the Asbestos Hazard Emergency Response Act mandatory course for the Asbestos Building Inspector Refresher and has passed an examination in that course with a minimum score of 70% or better. Training was in accordance with 40 CFR Part 763 (AHERA). The above student received the requisite training for asbestos accreditation under Title II of the Toxic Substances Control Act and State of Indiana requirements under 326 IAC 18-2 and Chapter 3701-34 Ohio Administrative Code.

	4/30/16	4/30/15	4/30/15	Columbus, OH
Training Manager	Expiration Date	Date(s) of Course	Examination Date	Course Location

TSI

33150 Lakeland Blvd.
Cleveland, OH 44095
1-866-666-8438

15 TSI 58782 ir



TSI Training Services International

Asbestos Management Planner Refresher

Certificate

This is to certify

Joseph D. Saunders

XXXX-XX-6484



has attended and successfully completed the Asbestos Hazard Emergency Response Act mandatory course for the Asbestos Management Planner Refresher and has passed an examination in that course with a minimum score of 70% or better. Training was in accordance with 40 CFR Part 763 (AHERA). The above student received the requisite training for asbestos accreditation under Title II of the Toxic Substances Control Act and State of Indiana requirements under 326 IAC 18-2 and Chapter 3701-34 Ohio Administrative Code.

4/30/16

4/30/15

4/30/15

Columbus, OH

Training Manager

Expiration Date

Date(s) of Course

Examination Date

Course Location

TSI

33150 Lakeland Blvd.
Cleveland, OH 44095
1-866-666-8438

15 TSI 58791 mpr



OHIO DEPARTMENT OF HEALTH

246 North High Street
Columbus, Ohio 43215

614/466-3543
www.odh.ohio.gov

John R. Kasich/Governor

Richard Hodges/Director of Health

June 11, 2015

Joseph D Saunders
3072 Southdale Drive #2
Kettering OH 45409

RE: Asbestos Hazard Evaluation Specialist
Certification Number: ES34837
Expiration Date: 06/10/2016

Dear Joseph D Saunders:

This letter and enclosed certification card approves your request to be certified as an Asbestos Hazard Evaluation Specialist. You must present your card upon request at any project site while performing duties. Copies of cards are not acceptable as proof of certification.

This certification may be revoked by the Director of Health for violation of any of the requirements of 3701-34 of the Ohio Administrative Code.

If you have any questions, please call Kathy Butcher, Licensure Specialist, at 614-644-0226.

Sincerely,

Bill Robbins, Section Chief
Bureau of Licensure Operations
Office of Health Assurance and Licensing

State of Ohio
Department of Health
Asbestos Program

Asbestos Hazard Evaluation Specialist



Joseph D Saunders
3072 Southdale Drive #2
Kettering OH 45409

DOB: 02/09/1956 Certification Number: **ES34837** Expiration Date: **06/10/2016**

This certification is issued pursuant to Chapter 3710 of the Revised Code and 3701-34 of the Ohio Administrative Code Certification Card is not valid if altered
